

69th Street and Western Avenue Expansion and Reconstruction

Project Information

- Contract Amount: \$6.2M
- Start Date: April 17, 2017
- Substantial Completion Date: October 27, 2017
- Final Completion Date: June 1, 2018

HR Green, Inc. is a private engineering firm hired by the City of Sioux Falls to provide construction updates and construction administration. Please contact the project team members with any questions or concerns.

Project Team

HR Green, Inc.
Craig Lauritzen, P.E.
 Project Manager
 Office: 605-221-2657
 Cell: 605-212-6051
 clauritzen@hrgreen.com

Kenny Van Ballegooyen
 Construction Observer
 Cell: 605-359-1705
 kvanballegooyen@hrgreen.com

City of Sioux Falls
Josh VandenBos, P.E.
 City Project Manager
 Office: 605-367-8619
 Cell: 605-929-1474
 jvandenbos@siouxfalls.org

D&G Concrete Construction, Inc.
Greg Branagh
 Project Manager
 Office: 605-338-8597
 Cell: 605-366-7743
 greg@dgconcrete.com

City of Sioux Falls Street
 Construction website:
<http://www.siouxfalls.org/public-works/street-construction>

If you'd like to receive future newsletters, send an email to tyorham@hrgreen.com or call 605.334.4499.

The entrance on Western Avenue to businesses along the northeast corner of 69th Street and Western Avenue is closed to allow for the construction and paving of the new driveway off Western Avenue. The driveway is scheduled to reopen to traffic on Monday or Tuesday next week, July 24th or July 25th, pending weather conditions. Access to the businesses will be maintained from the entrance on 69th Street.


Residents along the south side of 69th Street throughout the project should shut off all lawn sprinklers that are located in the boulevard. The contractor will begin removals along the south side of 69th Street and may damage sprinkler heads.

Progress to date:

- Concrete paving on the east half of Western Avenue, north of 69th Street to be completed this week.
- Crews have begun removals on the south side of 69th Street from Landau Circle to Western Avenue in Phase 2A.
- Northern Natural Gas has their contractor on site to install a new steel gas main under 69th Street along the west side of Western Avenue. The connection of the new gas main to the existing gas main is anticipated to be completed next week.
- Crews are installing new sidewalk along the north side of 69th Street.
- Electrical conduit is being installed for new street lights along the north side of 69th Street.

Upcoming work:

- Crews will continue removals on the south side of 69th Street from Landau Circle to Western Avenue in Phase 2A and move to begin removals on the south side of 69th Street from Western Avenue to Minnesota Avenue in Phase 2B.
- Underground utility work will begin on the south side of 69th Street.
- Crews will continue installing new sidewalk along the north side of 69th Street.
- Crews will be placing asphalt on Western Avenue, north of 69th Street and finishing asphalt on 69th Street from Lyncrest Avenue to Minnesota Avenue in Phase 1B.

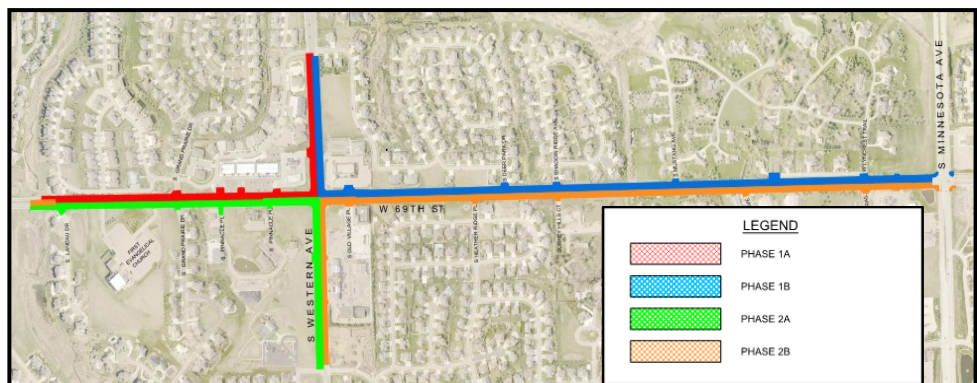

Map showing the phases of construction. The contractor will start working on portions of Phase 2A (green) and Phase 2B (orange). Phase 2A consists of work on the south side of 69th Street from Landau Circle east to Western Avenue and on the west side of Western Avenue from 69th Street south to La Quinta Street. Phase 2B consists of work on the south side of 69th Street from Western Avenue east to Minnesota Avenue and on the east side of Western Avenue from 69th Street south to La Quinta Street.
