

Madison Street and Louise Avenue Improvements

Project Information

- Contract Amount: \$4,336,798.82
- Start Date: April 2, 2018
- Completion Date: October 15, 2018

HR Green, Inc. is a private engineering firm hired by the City of Sioux Falls to provide construction services. Please contact the project team members with any questions or concerns.

Project Team

HR Green, Inc.
Dawn Horner, P.E.
Project Manager
Office: 605-334-4499
Cell: 605-351-2711
dhorner@hrgreen.com

Jennica Wilcox, P.E.
Project Engineer
Office: 605-221-2667
Cell: 719-351-4885
jwilcox@hrgreen.com

Derek Lee
Construction Observer
Cell: 507-370-3783
dlee@hrgreen.com

City of Sioux Falls
John Osman, P.E.
City Project Manager
Office: 605-367-8640
josman@siouxfalls.org

Contractor: D&G Concrete Construction, Inc.
Greg Branaugh
Project Manager
Office: 605-338-8597
Cell: 605-366-7743
greg@dgconcrete.com

City of Sioux Falls Street Construction website:
<http://www.siouxfalls.org/public-works/street-construction>

If you'd like to receive future bi-weekly newsletters, send an email to tgorham@hrgreen.com or call 605-334-4499.

Louise Avenue is fully closed to traffic from the Concrete Materials entrance to Madison Street to allow for work on the south half of Louise Avenue.

Madison Street is fully closed to traffic from Louise Avenue to Helen Avenue. East and westbound traffic shall use 12th Street as their primary route.

Progress to Date:


- Water main and storm drainage installation work is into the Madison Street and Louise Avenue intersection.
- Rock excavation is required to install both the water main and storm drainage pipe.
- Crews are grading the subgrade from Concrete Materials driveway east to the bridge on Madison Street.
- Construction of storm drainage intake and junction box structures on Madison Street.
- Epoxy coating and chip seal completed on the north half of Madison Street bridge deck.
- Removals completed on the south half of Louise Avenue.

Upcoming work:

- Continue water main and storm drainage installation in the intersection of Madison Street and Louise Avenue.
- Crews will begin installing water main and storm drainage from the intersection north on Louise Avenue.
- Epoxy coating and chip seal on the south half of the Madison Street bridge deck.
- Crews will be placing geogrid and gravel base on Madison Street from Concrete Materials driveway east to the Madison Street bridge.
- Concrete curb and gutter and paving on Madison Street from the Concrete Materials driveway east to the Madison Street bridge.



30" storm drainage pipe installed on Madison Street

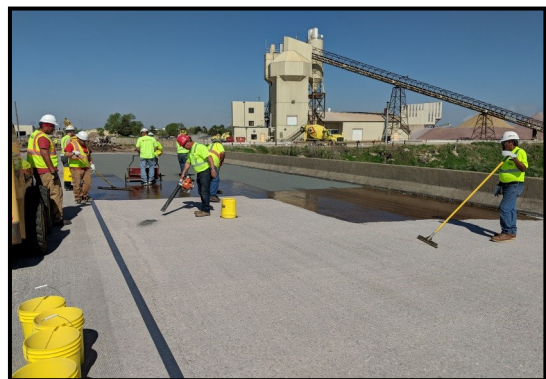

Crews placing a two-coat epoxy and chip seal on the Madison Street bridge. The chip seal gives the bridge surface a new wearing course to help with traction and preserve the life of the bridge deck.
